WIPP Update

Todd Shrader, Manager

Carlsbad Field Office Office of Environmental Management

South Carolina Governor's Nuclear Advisory Council Columbia, South Carolina April 13, 2017

WIPP Update

WIPP Background

- Location and geology
- Transportation system
- 2014 fire and radiological release events
- Key steps to recovery
- Recovery Challenges

WIPP Future - Near-Term (next 12 months)

- WIPP reopening
- Waste emplacement operations in Panel 7
- Resumption of shipping establishing priorities
- Supplemental Ventilation
- Restart of mining operations
- Mining and waste emplacement model
- Withdrawal from far south end of the WIPP underground

WIPP Future - Long-Term (1 to 5 years)

- New air intake shaft.
- New safety significant permanent ventilation system
- Conceptual model for additional disposal area


WIPP Geology

Facility mined in salt:

2,150 feet deep in ancient salt formation that closes in and entombs waste forever





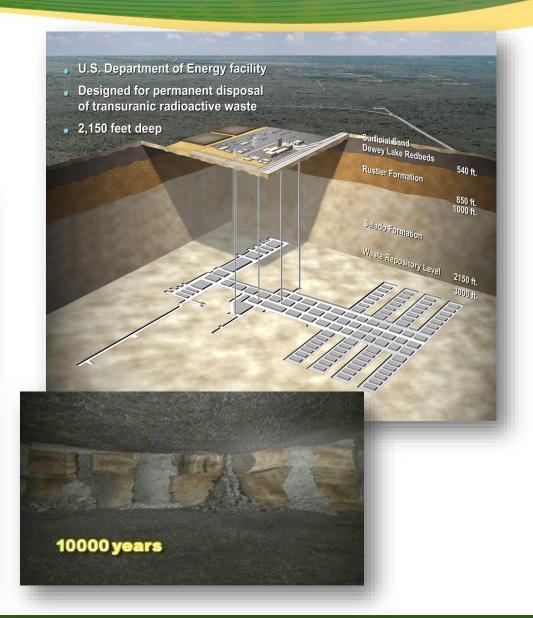

Disposal of "TRU" Waste at WIPP

- Materials contaminated with manmade radioactive elements heavier than uranium (mostly Plutonium)
 - Clothing, tools, rags, containers, etc.
 - Soils and debris
 - Homogeneous solids, residues
- > 100 nCi/g (~1ppm):
 - alpha emitting isotopes
 - $t\frac{1}{2} > 20$ years
- Two types of TRU waste
 - Contact-Handled (<200 mrem/hr)
 - Remote-Handled (>200 mrem/hr)
- Legacy inventory ~700,000 drum equivalents




1	Periodic Table											II.A	IVA	VA.	VIA	VIA	0 He	
2	Li	of the Elements									B	°c	H	0	F	No		
3	Νa	Mg	118	IYB	٧B	VIВ	VIIB	_	- VII -		IB	IB	AI.	Si	P	5	CI	Ar
4	19 K	Ca.	Se	Ti	×	Cr	Mn	Fe	Co	Ni Ni	Cu	Zn	Ga	Ge	Ac Ac	Se Se	95 Br	30 Kr
s	37 Я Ь	Sr	Y	Zr	Nb Nb	Mo	Tc	el Ru	6 Ah	e Pd	Ag	Cd	in in	50 Sn	Sb	Te	53	S4 Xe
6	Cs	Ba.	M.a	H	Ta	**	Re	Os	'n	Pt	AU	Hg	TI	PD	63 B1	Po	Až	Rn
7	Fr	Ra.	•Ac	RF	Ha Ha	106 8g	Ns Ns	Hs	Mt	110	***	112	113					

*Lanthanide	50	50	60	61	12	67	64	65	66	67	6.0	69	70	71
Series	Ce	Pr	No		-	Eu	Gu	IU	D /	Diam'r.	T.		TD	
+ Actinide Series	, Th	Pa	41	Np	Pu	Åm	Čm	Bk	Cf	Es	Fm	P	No	Lr

TRU Waste Characterization

Process to determine the physical, chemical and radiological contents of TRU waste containers to ensure that waste is acceptable for disposal at WIPP

Acceptable Knowledge



Use documented waste stream knowledge to identify waste contents

Real Time Radiography



Look for prohibited items, such as aerosol cans or liquids

Nondestructive assay




Determine radiological contents

Statistical headspace gas analysis



Determine volatile organic compound contents

Statistical solids sampling & analysis



Performed on samples of homogeneous waste to analyze for chemical hazards

WIPP Transportation System

NRC certified Type B containers:

TRUPACT III
TRUPACT III
RH-72B



WIPP Transportation System




WIPP Transportation System



Waste containers are loaded into protective shipping containers (such as TRUPACT-II)



Shipping containers are loaded onto specially designed flatbed trailers.
State personnel inspect load before departure



Drivers inspect their rigs and loads every 3 hours or 150 miles. Some states require additional inspections at their ports of entry



For safety and security reasons, shipments are tracked throughout their journey using a satellite system (TRANSCOM)



WIPP-trained state and local emergency responders along all shipping routes, with frequent exercises

WIPP Regulatory Framework



U.S. Environmental Protection Agency (EPA)

Repository certification, radionuclide regulation, PCBs

New Mexico Environment Department (NMED)

RCRA hazardous constituents, water discharge, groundwater, air



U.S. Nuclear Regulatory Commission (NRC)

Transportation Type B packages for nuclear materials



Mine and Occupational Safety and Health Administrations Worker Safety and Health



Highway transportation, Type A containers

The February 2014 Accidents at WIPP



WIPP incidents

February 5, 2014 Truck Fire:

- All operations at the repository ceased following salt haul truck fire in the WIPP underground.
- An investigation team was deployed to determine the cause of the fire.

February 14, 2014 Radiological Incident:

- A continuous air monitor detected airborne radiation in the underground.
- WIPP's ventilation system automatically switched to high-efficiency particulate air (HEPA) filtration mode when airborne radiation was detected
- Underground and the WIPP mine remains in filtration mode at this time.
- Extensive sampling and monitoring conducted by DOE, New Mexico, and Carlsbad Environmental Monitoring Research Center
- Efforts by the DOE and Nuclear Waste Partnership are ensuring workers are fully protected during recovery and restart.

Truck Fire and Radiological Release

February 5 Underground Fire




Accident Investigation Board (AIB) Report issued March 13, 2014

February 14 Radiological Release



- AIB Report, Phase I issued April 24, 2014
- AIB Report, Phase II issued April 16, 2015

Recap of Incidents: Layout of the Underground

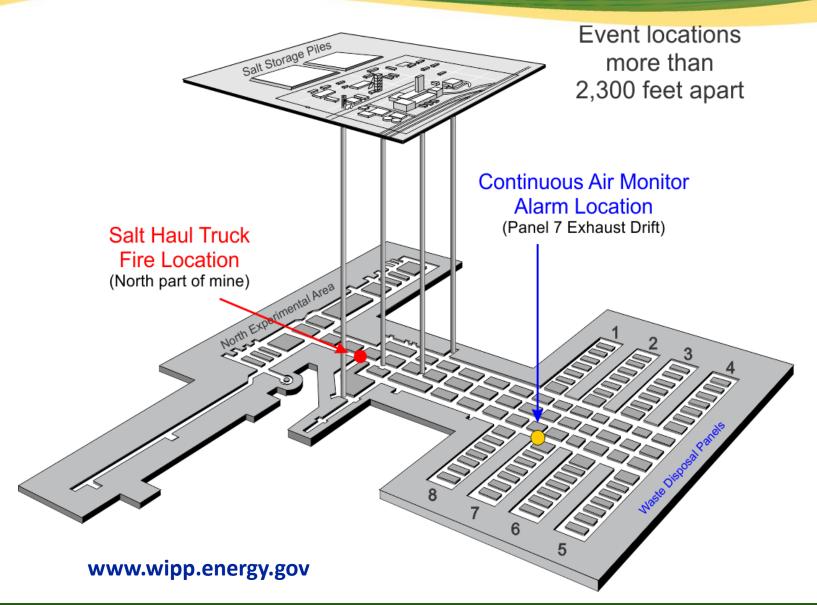

Key Steps Toward Recovery

- Documented Safety Analysis Revisions
- Safety Management Program Revitalization
- Underground Restoration
 - Re-Establish Degraded Equipment
 - Fire Protection
 - Maintenance and Ground Control
 - Radiological Roll-back
 - Soot cleaning of electrical panels
- Expedite mine stability
- Initial Panel 6 and Panel 7, Room 7
 Closure
- Interim Ventilation






Key Steps Toward Recovery

- Initial Panel 6 and Panel 7,
 Room 7 Closure isolation of nitrate salt waste
- Procurement and installation of Interim Ventilation System





Radiological Conditions

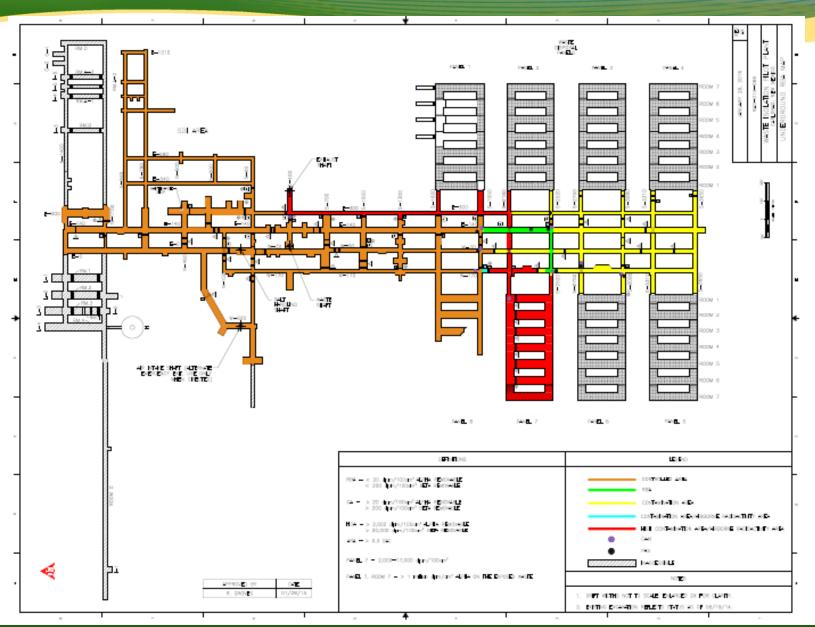


Ground Control Challenges

Limitations:

- 9 months with no ground control following incidents
- Low ventilation rates limited bolting operations
- Need for workers to operate in personal protective clothing and respirators



Ground Control Status

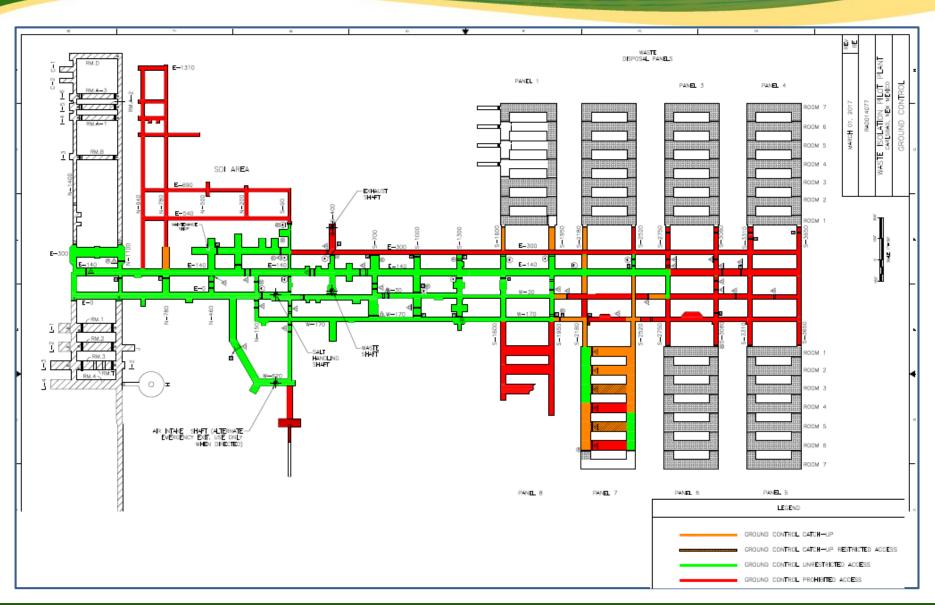

Reopening and Resumption of Shipments



Reopening



WIPP Officially Reopened with a ribbon cutting ceremony held on January 9, 2017


Waste Emplacement Resumes



- Waste emplacement operations resumed in Panel 7 transition point between clean and contaminated area is necessary
- Most of the stranded waste from the Waste Handling Building has been emplaced – remaining waste streams need further evaluation for oxidizers

Panel 7 Status

- Bulkhead were placed at both ends of Room 7 to isolate waste following events – remains closed
- Rock fall occurred in Room 4 on November 3, 2016 – fall was predicted and room was already prohibited
- Room 6 is prohibited due to ground control – also contains abandoned equipment
- Rooms 1, 2, 3 and 5 are safe and usable for waste emplacement
- Waste emplacement has started in \$2520 moving west to east
- Currently available disposal capacity in Panel 7 should last approximately 3 years, depending on shipping rates

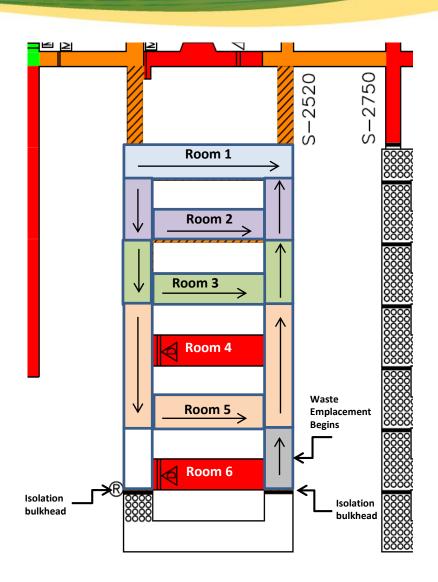

Timing and Origin

Shipments resumed earlier this month -

- First shipment was received from Idaho on April 8
- Shipment rate of 2/week ramping up to 4/week by the end of 2017
- WIPP anticipates receipt of approximately 128 shipments between April of 2017 and the end of January 2018
- First group of shipments is expected to be from Idaho and Savannah River and Waste Control Specialists – not necessarily in that order
- Additional shipments are expected from Los Alamos National Lab and Oak Ridge National Lab later in 2017



Projected Shipping Estimates

Key considerations in the development of the shipping estimate and points of origin included:

- WIPP waste emplacement rate;
- Available waste to ship;
- Regulatory commitments and agreements;
- WIPP transportation/waste acceptance capabilities;
- Flexibility for changing technical and policy constraints.

Site	Projected Shipments
Idaho	61
Los Alamos	24
Oak Ridge	24
Savannah River	8
Waste Control Specialists	11
TOTAL	128

Factors Affecting Shipping Priorities

Shipping priorities are based on many factors, including:

- Need to mix of waste streams from around the complex to avoid concentration of VOC generating waste in one location
- Need to mix waste types to manage curie limits for the Waste Handling Building during processing
- Need to receive packages that can be stacked in a manner that maximizes use of limited disposal area



Supplemental Ventilation/De-dusters

Supplemental Ventilation
System (SVS) will add 70
KCFM to underground to
support mining operations
– on line in late September



Use of new "de-dusting" technology should reduce impacts of salt dust on air filtration systems

Mining Panel 8 Will Resume


Mining of Panel 8:

- Planned to begin in October 2018
- No contamination present
- Required to bolt our way into the panel to remove equipment that has remained there since events
- Mining operations are expected to take approximately 3 years



WIPP Mining and Waste Emplacement Model

Waste Emplacement Rates FY17 - FY23

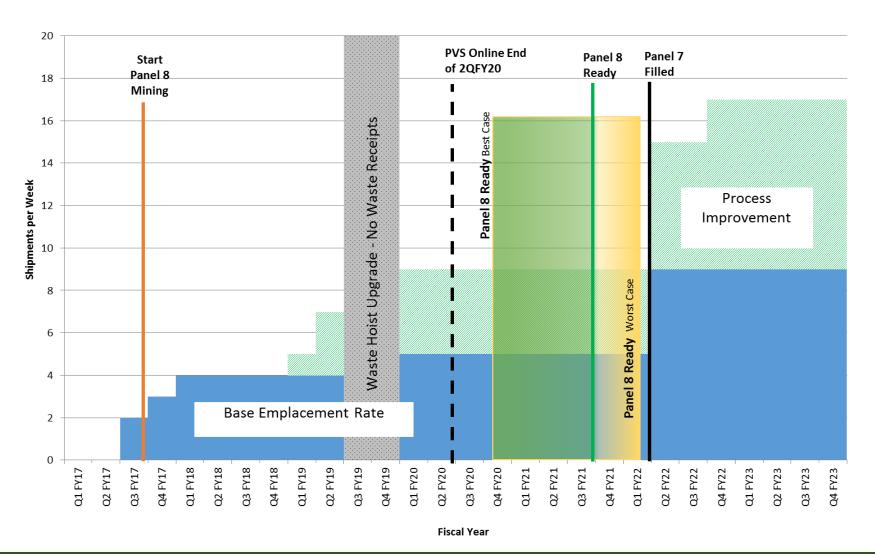

Far South End Closure Progress

NASTE DISPOSAL PANELS

- Initiated preparations for the withdrawal from the far south end (Panel 9)
- Cribbing, ventilation curtains and geomechanical instrumentation installed in the south mains by June 2017
- Regulatory approvals for final closures;
 2+ years with implementation to follow




New Ventilation Shaft

- Using top-down drilling method
- Located across the access road from the WIPP parking lot
- Geotechnical core drilling to 2,300 feet is complete
- Critical Decision 2/3 expected in March 2018



Depiction of New Footprint

- New footprint is being evaluated with the following criteria:
 - ✓ Priority will be to create panels to compensate for authorized disposal area that was reduced by ground control issues in the far south end
 - ✓ Panels and drifts construction is under review
 - ✓ Panels will be mined with existing equipment and methods

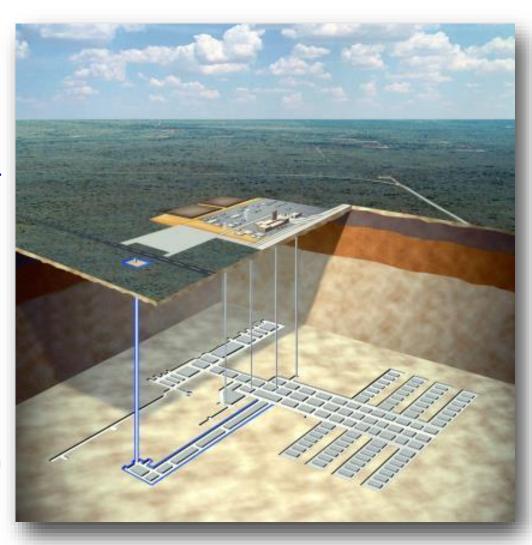

Permanent Ventilation System


New filter building

New safety significant confinement system connected to the existing exhaust shaft through a salt reduction facility and then to a new Filter Building with HEPA filters and exhaust fans -

Currently at 90% design

CD 2/3 is expected in March 2018

CD 4 December 2020

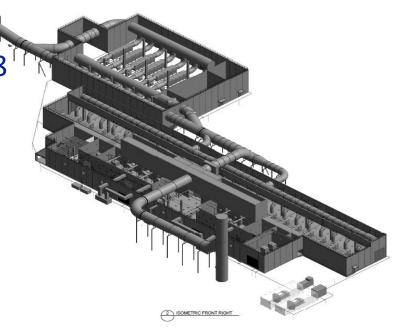

Questions &

Answers











WIPP Underground Map

